

Executive Summary — Plant, Ductwork & Seismic Bracing

Works completed by SA Quality Ductwork for the reporting week, issued to Climatech.

PROJECT The Garema Hotel (5-Star), ACT	PRINCIPAL CONTRACTOR TP Dynamics	MECHANICAL CONTRACTOR Climatech	SITE SUPERVISOR Keith Morgan
WORKS BY SA Quality Ductwork	REPORTING PERIOD Thu 20 – Wed 26 Aug 2026	SITE CREW P. Agosto, L. Taipe, Eduardo, Anthony	PREPARED BY P. Agosto & L. Taipe

01 SCOPE OF WORKS DELIVERED

- Support steelwork — trapeze and goal-post frames installed and levelled (PH-02, 03, 05).
 - Unit setting — VRV modules and FXSQ fan coils set on AV mounts (PH-04, 06, 11, 15).
 - Plenums — hung on AV hangers with flexible connections (PH-10).
 - Ductwork — insulated duct, transitions and damper sets (PH-08, 09, 12).
 - Seismic bracing — braces changed out to direction (PH-13, 26).
- Ground Floor to Level 1 — duct run installed and connected.
 - Level 1 to scaffold — parts changed out from the EWP (PH-25, 26).
 - Ground Floor to Basement 3 — all ductwork taken down and re-stored (PH-23, 24).
 - Relocation — plant moved to the rooftop store, balance covered (PH-16 to PH-22).
 - Materials — duct, dampers and fixings received and staged (PH-01).

02 PROGRESS BY WORK FRONT

WORK FRONT	WORKS PERFORMED	QTY	STATUS
Plant room / riser	Frames installed; VRV modules set on AV mounts and levelled	—	COMPLETE
Typical floors	Ducted FCUs and plenums hung; connection points presented	—	COMPLETE
Typical floors	Seismic braces changed out to supervisor direction	—	COMPLETE
Soffit & risers	Insulated duct runs, damper sets and boxes to drawings	—	IN PROGRESS
Ground Floor – L1	Duct run installed and connected between the two levels	—	COMPLETE
Level 1 / scaffold	Parts changed out at the soffit, worked from the EWP	—	COMPLETE
GF – Basement 3	All Ground Floor ductwork taken down and re-stored in B3	—	COMPLETE
GF store / rooftop	Plant relocated to the rooftop store; balance covered	—	COMPLETE
Soffit anchors	Anchors inspected and marked — OK / X for replacement	—	DIRECTION REQ.

03 COORDINATION & OBSERVATIONS

- OPEN ITEM — CONCRETE ANCHORS

Soffit anchors are still being found stripped or not holding. Marked on the slab — compliant circled OK, defective marked X (PH-14). HKD drop-ins recommended before further hanging.
- Seismic bracing — braces changed as directed; fixings depend on the anchors above.
 - Insulation — made good at supports; permanent reinstatement to be programmed.

04 SAFETY & COMPLIANCE

- All crew inducted; works under the site SWMS with daily pre-start and toolbox attendance.
- Height work from EWP and approved platforms. No injuries or incidents recorded.

05 PLANNED WORKS — NEXT PERIOD

- Finish plenum hanging and flexible connections at the remaining floors.
- Replace defective anchors with HKD drop-ins, subject to direction.
- Continue duct runs, damper sets and access panels; progressive sign-off.

Pablo Agosto & Lewis Taipe
SA Quality Ductwork

SIGNATURE / DATE

Keith Morgan
Climatech

SIGNATURE / DATE



MATERIALS

Basement material store

Duct, dampers and plenums received, checked and staged clear of access routes.



SUPPORT STEEL

Support frames, plant area

Trapeze and goal-post frames installed to slab and soffit, levelled to the unit footprints.



SUPPORT STEEL

Frame run set out

Frames held to a common line and level so connections and clearances stay uniform.



UNIT SETTING

Daikin RWEYQ10TYM set

Water-cooled VRV module, Ser. E001506, positioned and seated on its frame.



VIBRATION

AV pads at unit base


Rubber pads between base rail and steel so the unit bears fully on the isolator.



UNIT SETTING

Water connection presented

Condenser water connections capped and presented clear for the hydraulic trade.

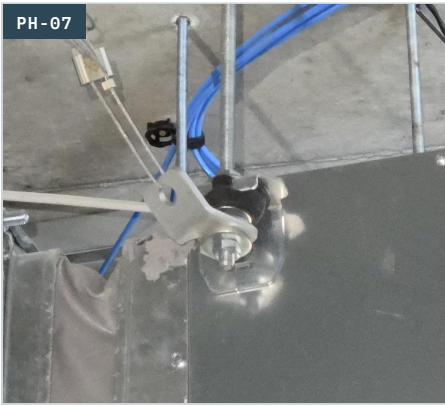

BRACKETRY

Bracket fixed and tightened

Wall bracket tensioned; refrigerant and control cabling dressed to saddles.



DUCTWORK

Insulated duct transition

Insulated duct and spiral transition on unistrut, set clear of the services above.



DUCTWORK

Riser duct and damper

Riser duct on threaded rod with damper set; insulation made good at the support.

PHOTOGRAPHIC RECORD

SECTION B – HANGING, SEISMIC BRACING, ANCHORS & RELOCATION

Works Summary Report 02

THE GAREMA HOTEL · 20-26 AUG 2026



HANGING

Plenum hung to soffit

Plenum on threaded rod with rubber-in-shear hangers and flexible connection.



UNIT SETTING

Ducted FCU hung

Daikin FXSQ fan coil on four rods; refrigerant, drain and electrical points left accessible.



DUCTWORK

Duct run to drawings

Plenum, filter box and spiral to the issued set, open ends protected.



SEISMIC

Seismic braces changed

Restraint cables and braces changed out to direction; cabling and drain redressed.



OPEN ITEM

Anchors marked on slab

Compliant anchor circled OK, defective marked X. HKD drop-ins recommended.



VIBRATION

AV hanger detail

Rod double-nutted at the bracket with a rubber pad between clamp and bracket.



DIRECTION

Items marked for relocation

Filtration skid, control panel and cartons marked up at the Ground Floor store.



DIRECTION

Pallet marked to stay


Protection matting and fixings marked to stay on site and be covered.



RELOCATION

Relocated to rooftop


Marked items set down in the agreed rooftop location, clear of the duct run.

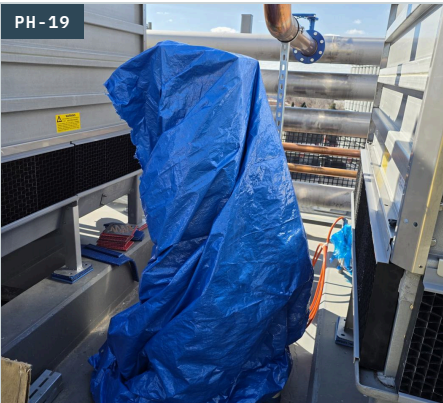

PROTECTION

Stored plant covered


Relocated plant covered on the rooftop deck, clear of walkways.

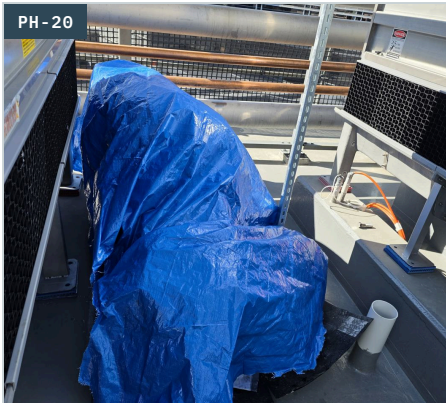

PROTECTION

Second pallet covered


Balance covered and weighted down against wind exposure.

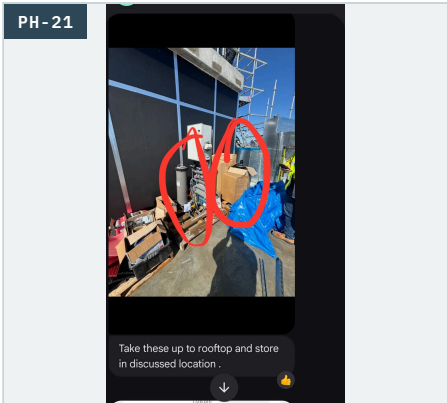

DIRECTION

Rooftop transfer

26/08: marked items to be taken to the rooftop and stored in the agreed location.

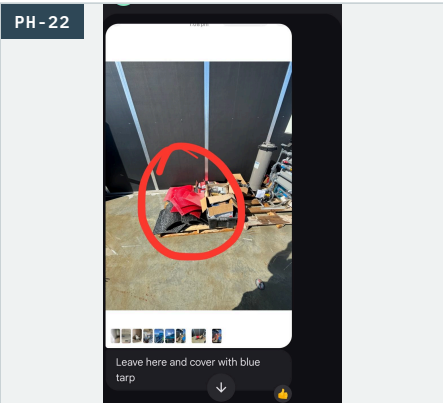

DIRECTION

Cover in place

26/08: marked pallet to be left in place and covered with tarpaulin.



RELOCATION

Ductwork down to Basement 3


All Ground Floor ductwork taken down and re-stored in Basement 3.



RELOCATION

Plenums stored in B3


Plenum boxes stacked with ends wrapped, clear of plant and access.

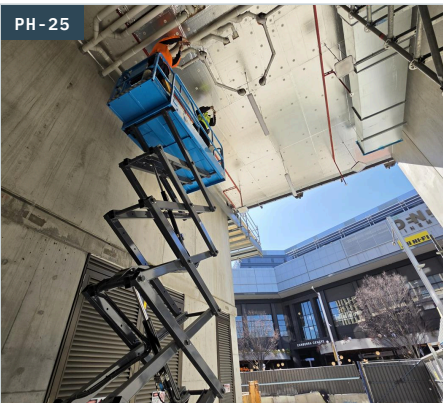

ACCESS

EWP set up at Level 1

Scissor lift set up for the changeover between Level 1 and the scaffold.

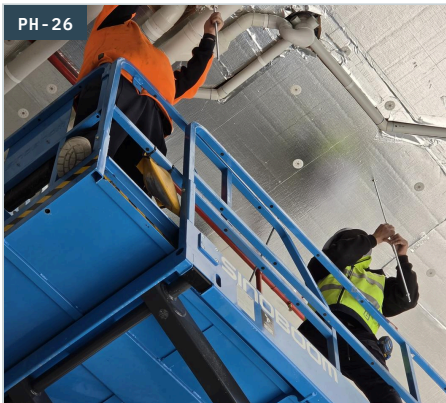

SEISMIC

Parts changed from the EWP

Braces and fixings changed out at the soffit from the platform.

06 DIRECTION & DISTRIBUTION

Rooftop transfer — 26/08

“Take these up to rooftop and store in discussed location.” Actioned same day (PH-16, 18–21).

Cover in place — 26/08

“Leave here and cover with blue tarp.” Actioned same day (PH-17, 22).

Issued to

Keith Morgan (Climatech), TP Dynamics site management, project file. Quantities and levels to be read with the daily docketts.

Pablo Agusto & Lewis Taipe
SA Quality Ductwork

SIGNATURE / DATE

Keith Morgan
Climatech

SIGNATURE / DATE
